MDM GRC READINESS & CONTROL ASSURANCE CASE STUDY

MDM-D13

GRC Workspace and Readiness Dashboard

Deliverable 13 of 15 in a portfolio case study on readiness and control assurance for mobile access to Microsoft 365 at a fictional 850-employee Saudi financing company. Cross-references to other deliverables use their MDM-D numbers.

Prepared by
Ali Fathi Aldhabiki
Cybersecurity Governance, Risk & Compliance (GRC)
linkedin.com/in/ali-aldhabiki-a74354212 | ali.f.aldhabiki@outlook.com

Notice
The organization is fictional. No Microsoft Intune or Entra ID tenant was configured; all evidence, test results and ratings are simulated.

GRC Workspace and Readiness Dashboard

MDM-D13

1. Purpose and Scope

This document shows where the MDM case study stands, and how its records link together. It adds no new risk ratings or Risk Owner decisions. Its only new judgements are the control readiness ratings that MDM-D10 assigns to this document, and the overall readiness status. Both follow fixed rules in Section 3. Every figure in it comes from MDM-D04 and MDM-D09 to MDM-D12, with a reference to the section it came from.

It has two parts. The workspace part sets out the registers, how their IDs link, and who updates each one. The dashboard part defines the readiness measures and reports them as at 16 November 2026, the date of the Risk Owner decisions in MDM-D12.

The dashboard is a reporting view, not a source. Where it differs from a source document, the source is correct and the dashboard is fixed.

MDM-D13 feeds MDM-D14. The overall readiness status in Section 4 is the starting point for the executive report.

MDM-CTL-006, MDM-CTL-008 and the MDM-D07 requirements outside the MDM-D10 sample were not tested, as stated in MDM-D12. The dashboard shows them as coverage gaps so they are not read as passed.

No tenant was configured and no dashboard tool was built. The dashboard is a document view, and all values are simulated.

Structure

Section	Content	Main Sources
1. Purpose and Scope	Purpose, scope and structure of this document	None
2. Workspace Structure	Registers and ID scheme, the traceability chain from asset to decision, and update rules	MDM-D03 to MDM-D12
3. Readiness Measures	Each measure with its calculation, source and thresholds, and the rules for control readiness and the overall readiness status	MDM-D04, MDM-D09 to MDM-D12
4. Readiness Snapshot	The overall status as at 16 November 2026, the measures, control readiness, open decisions, milestones and items for attention	MDM-D09 to MDM-D12
5. Reporting and Escalation	Who receives the dashboard, how often, and what is escalated	MDM-D02, MDM-D12 Section 6
6. Assumptions and	What the dashboard assumes and what it	None

Section	Content	Main Sources
Limitations	cannot show	

2. Workspace Structure

The workspace is ten registers linked by ID. Any item can be traced from the asset at risk to the decision taken on it, and back.

2.1 Registers and IDs

Register	ID Format	Held In	Prepared By	Approved or Decided By
Assets	MDM-AST-001	MDM-D03	GRC Analyst	CISO
Risks	MDM-RSK-001	MDM-D04; residual fields updated from MDM-D12	GRC Analyst	CISO; Risk Owner for treatment and targets
Controls	MDM-CTL-001	MDM-D05	GRC Analyst	CISO
Standard requirements	MDM-STD-001	MDM-D07	GRC Analyst	CISO
Conditional Access policies	MDM-CAP-001	MDM-D08	GRC Analyst	CISO
Evidence	MDM-EVD-001	MDM-D09	IT Operations Team, or the enterprise IAM team for the items listed in MDM-D09 Section 2.2	GRC Analyst rates each item Accepted, Partial or Not Provided
Tests	MDM-TST-001	MDM-D10	GRC Analyst	CISO
Findings	MDM-FND-001	MDM-D11	GRC Analyst	Control Owner agrees the finding
Recommendations	MDM-REC-001	MDM-D11; retest plan in MDM-D12 Section 5	Owner named in each recommendation	Closed by a passed retest (GRC Analyst or Internal Audit)
Risk Owner	D-nn	Raised in MDM-	GRC Analyst	Business Owner

Register	ID Format	Held In	Prepared By	Approved or Decided By
decisions		D11 Section 6; recorded in MDM-D12 Section 3		

Preparer and approver follow the MDM-D02 RACI: the GRC Analyst is Responsible and the CISO Accountable for scope, risks, control requirements and testing. Simulated evidence files carry their own reference, such as SIM-EVD-001, inside their MDM-EVD record.

Assumption and limitation IDs (A-, L-, AS-, LM-) are local to the document that holds them. They are always cited with that document, for example MDM-D08 A-06.

2.2 Traceability Chain

Each link in the chain is held in one place. The dashboard reads the links from there and keeps no copy of its own.

Link	Recorded In
Asset → Risk	MDM-D04, Related Assets field of each risk
Risk → Control	MDM-D05, each control entry
Control → Evidence	MDM-D09 Section 3, evidence requests by control
Evidence → Test	MDM-D09 Section 4, D10 Test column of the evidence index
Test → Finding	MDM-D11 Section 3, Test, Control and Risk columns of the register
Finding → Recommendation	MDM-D11 Section 5, Finding column
Recommendation → Decision, Residual and Retest	MDM-D12 Sections 3 to 5

Broken links are reported, not filled in. MDM-FND-007, 008 and 009 have no control in MDM-D05 and no risk in MDM-D04, so each is rated against the closest risk. MDM-TST-008 to 010 test MDM-D07 requirements that have no risk in MDM-D04. Section 3 measures these breaks as chain completeness.

2.3 Worked Example

One full chain, for the iOS Share extension finding.

Step	Item	What the Record Shows
Asset	MDM-AST-006	Personal iOS/iPadOS devices used for work
Risk	MDM-RSK-002	Corporate data leakage to personal apps or accounts. Inherent High (12). Risk Owner: Business Owner
Control	MDM-CTL-002	Its requirements sit in MDM-D07 Sections 4.2–4.5 (MDM-STD-010 to 013)
Evidence	MDM-EVD-005	iOS app protection policy export, rated Accepted
Test	MDM-TST-001	BYOD data transfer restrictions
Finding	MDM-FND-001	iOS Share extension moves corporate files outside managed apps. Design, Medium (8)
Recommendation	MDM-REC-001	Record the platform constraint in MDM-D07 Section 4.4 and submit the remaining exposure to the Business Owner. Owner: IT Operations Manager
Decision	D-02	Accepted on 16 November 2026, on condition that shared files cannot be opened outside managed apps
Residual and Retest	MDM-RSK-002	Current Medium (9), provisional. Target Medium (8). MDM-REC-001 retest by 14 February 2027

2.4 Update Rules

Rule	Description
UR1 – Source first	A value changes in its source register first. MDM-D13 is then updated from the source, never the other way round.
UR2 – Dated snapshot	Every snapshot shows its as-at date. A new snapshot replaces the old one in Section 4, and the old one stays in the version history.
UR3 – Refresh	The snapshot is refreshed on the cadence in Section 5, and after any event in MDM-D12 Section 6.
UR4 – Approval	The GRC Analyst prepares each snapshot and the CISO approves it before it is shared, as MDM-D02 sets for reporting readiness conclusions.

Rule	Description
UR5 – Independence	Where GRC prepared the item itself, such as MDM-REC-009, the dashboard shows the Internal Audit result, not a GRC status.
UR6 – Simulation	Every snapshot is labelled simulated while no tenant exists.

3. Readiness Measures

Readiness is judged on nine measures in two groups. Coverage measures show how much of the scope has been assessed. Outcome measures show how well the assessed scope works. A Red outcome measure makes the case Not Ready. A coverage measure below Green stops it from being Ready.

3.1 Coverage Measures

ID	Measure	Calculation	Source	Green	Amber	Red
RM-01	Risk assessment coverage	Risks with a current residual ÷ risks in MDM-D04	MDM-D12 Section 4	100%	75–99%	Below 75%
RM-02	Control test coverage	MDM-D05 controls tested in MDM-D10 ÷ controls in MDM-D05	MDM-D10 Sections 3.1 and 5	100%	75–99%	Below 75%
RM-03	Requirement test coverage	MDM-D07 requirements covered by an MDM-D10 test ÷ requirements in MDM-D07	MDM-D10 Sections 3.1 and 5	100%	75–99%	Below 75%
RM-04	Evidence acceptance	Evidence items rated Accepted ÷ evidence items requested	MDM-D09 Section 4	95% or more	80–94%	Below 80%
RM-05	Chain completeness	Findings linked to both a control in MDM-D05 and a risk in MDM-D04 ÷ findings	MDM-D11 Section 3	100%	80–99%	Below 80%
RM-06	Open Risk Owner decisions	Decisions not yet made or not yet in effect	MDM-D12 Section 3	None open	Open, each tied to a dated retest or assessmen	Open with no date

ID	Measure	Calculation	Source	Green	Amber	Red
					t	

3.2 Outcome Measures

ID	Measure	Calculation	Source	Green	Amber	Red
RM-07	Control effectiveness	Tests rated Effective ÷ tests performed. A test counts as Effective once every recommendation linked to it passes retest	MDM-D10 Section 3.3; MDM-D12 Section 5	90% or more	70–89%	Below 70%
RM-08	Residual risk profile	Assessed risks with a current residual of High	MDM-D12 Section 4	None, and none provisional	None, but at least one provisional	One or more
RM-09	Remediation timeliness	Recommendations past their due date and not closed	MDM-D11 Section 5; MDM-D12 Section 5	None overdue	None overdue, but one or more due within 30 days and not yet reported complete	One or more overdue

3.3 Overall Readiness Status

The status is set by the first rule that applies.

Order	Status	Rule
1	**Not Ready**	Any outcome measure (RM-07 to RM-09) is Red.
2	**Ready**	Every measure is Green.
3	**Ready with Conditions**	All other cases. The conditions are the measures below Green, listed in Section 4.

The status describes the tested scope only. The coverage measures show what lies outside it, so a reader cannot take an untested area as passed.

A measure that relies on a provisional value, such as the MDM-RSK-002 residual, is marked provisional. So is the overall status, if it would change when that value changes.

Coverage reaches Green only at 100%, because an untested area cannot be called ready. Amber at 75% marks a scope that is mostly tested, with the rest planned for the next cycle. The 90% effectiveness line allows one test in a sample of ten to fall short.

3.4 Control Readiness Rating

MDM-D10 assigns the control rating to this document. Each control in MDM-D05 is rated from its MDM-D10 test results.

Rating	Rule
Implemented	Every test of the control is Effective, or has become Effective after a passed retest (RM-07).
Partial	The control's tests give mixed results, or a test is Partially Effective.
Not Implemented	Every test of the control is Not Effective.
Not rated	The control was not tested. It counts against RM-02 instead.

The rating shows how the control performed when tested, not whether a configuration exists. Tests of MDM-D07 requirements with no control in MDM-D05 (MDM-TST-008 to 010) are not rated here. They count in RM-05 and RM-07.

4. Readiness Snapshot

As at 16 November 2026, the case is Not Ready. Two of ten tests were effective, so the tested controls cannot yet be relied on. No assessed risk sits at High and no recommendation is overdue. All values are simulated.

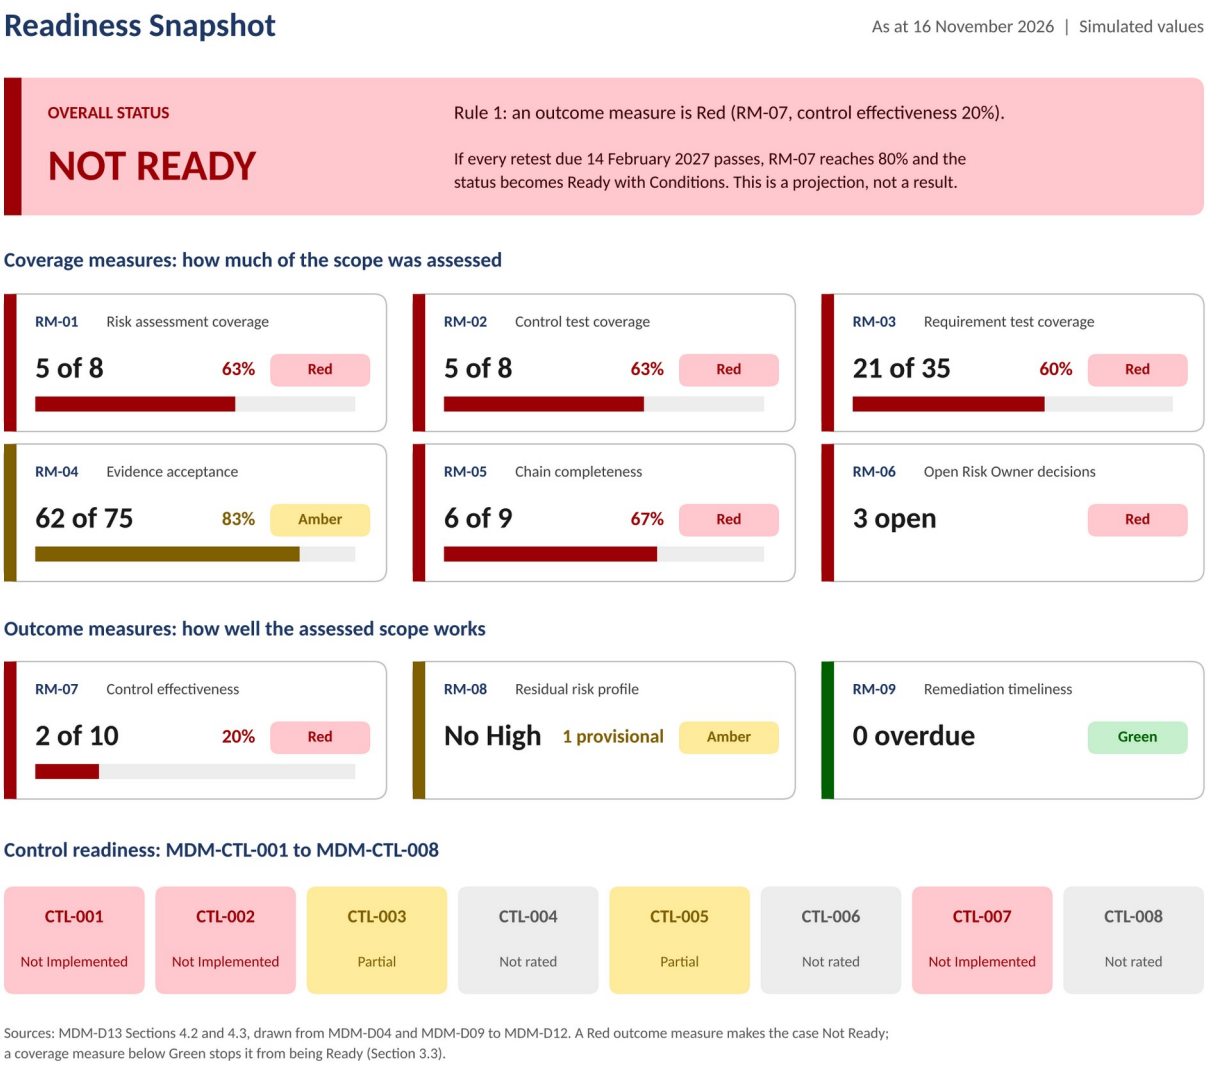


Figure 1. Readiness snapshot as at 16 November 2026. Values come from Sections 4.2 and 4.3. All values are simulated.

4.1 Overall Status

The status is Not Ready under rule 1 in Section 3.3, because RM-07 is Red. It is not provisional: a change in the MDM-RSK-002 residual would not change it.

If every retest due by 14 February 2027 passes, MDM-TST-001, 002, 005, 006, 007 and 008 count as Effective. RM-07 would then reach 8 of 10 (80%, Amber), and the status would become Ready with Conditions. This is a projection, not a result.

Ready needs every coverage measure at 100%. That depends on the next test cycle, which has no date yet (Section 4.5).

4.2 Measures

ID	Measure	Value	Status	Basis
RM-01	Risk assessment coverage	5 of 8 (63%)	Red	MDM-RSK-004, 006 and 008 not assessed
RM-02	Control test coverage	5 of 8 (63%)	Red	MDM-CTL-004 not tested (MDM-EVD-023 Not Provided); MDM-CTL-006 and 008 left to the next cycle
RM-03	Requirement test coverage	21 of 35 (60%)	Red	14 untested: MDM-STD-009, 014 to 021, 024, 026, 027, 030 and 031
RM-04	Evidence acceptance	62 of 75 (83%)	Amber	9 Partial, 4 Not Provided
RM-05	Chain completeness	6 of 9 (67%)	Red	MDM-FND-007, 008 and 009 have no control in MDM-D05 or risk in MDM-D04
RM-06	Open Risk Owner decisions	3 open	Red	D-01 has no date. D-03 and D-04 are tied to retests due 14 February 2027
RM-07	Control effectiveness	2 of 10 (20%)	Red	Effective: MDM-TST-004 and 010
RM-08	Residual risk profile	No High; 1 provisional	Amber	MDM-RSK-002 at Medium (9), provisional until MDM-REC-011
RM-09	Remediation timeliness	None overdue	Green	Earliest due date 14 February 2027

MDM-STD-009 (MDM-D07 Section 4.1) is covered by no MDM-D10 test and is missing from the untested list in MDM-D10 Section 5. It is counted as untested here.

MDM-REC-010 brings MDM-CTL-004 and MDM-RSK-004 into testing. If it is done by 14 February 2027, RM-01 and RM-02 each reach 6 of 8 (75%, Amber).

4.3 Control Readiness

Control	Tests	Results	Rating
MDM-CTL-001	MDM-TST-006	Not Effective	Not Implemented
MDM-CTL-002	MDM-TST-001, 002	Not Effective; Not Effective	Not Implemented
MDM-CTL-003	MDM-TST-005	Partially Effective	Partial
MDM-CTL-004	None	Not tested; MDM-EVD-023	Not rated

Control	Tests	Results	Rating
		Not Provided	
MDM-CTL-005	MDM-TST-003, 004	Not Effective; Effective	Partial
MDM-CTL-006	None	Next test cycle	Not rated
MDM-CTL-007	MDM-TST-007	Not Effective	Not Implemented
MDM-CTL-008	None	Next test cycle	Not rated

No control is rated Implemented yet. Three are Not Implemented, two Partial and three not rated.

4.4 Open Decisions and Milestones

Date	Milestone	Effect on the Dashboard
14 February 2027	Retests of MDM-REC-001, 002, 004 to 007 and 009 to 012; first quarterly review under MDM-REC-003	If all pass, RM-07 reaches 80% and the status becomes Ready with Conditions. MDM-REC-005 settles D-03, MDM-REC-011 settles D-04, and MDM-REC-010 brings MDM-RSK-004 into assessment
15 May 2027	MDM-REC-008 retest	MDM-TST-009 counts as Effective
After the second quarterly review	MDM-REC-003 closure, validated by Internal Audit	MDM-TST-003 counts as Effective, and MDM-CTL-005 can reach Implemented
Not set	IT Operations assessment for D-01	A date moves RM-06 from Red to Amber
Not set	Next test cycle: MDM-CTL-006, MDM-CTL-008 and the untested MDM-D07 requirements, MDM-D07 Section 5.2 first	Needed for any coverage measure to reach Green

4.5 Items for Attention

These items come from building the dashboard. They are reported to the CISO under Section 5. The dashboard does not decide them.

Item	Why It Matters	Raised With
D-01 has no date for the IT Operations assessment	MDM-RSK-003 target stays open, and RM-06 stays Red	Business Owner, through the CISO
The next test cycle has no date	No coverage measure can reach Green, so the case cannot reach Ready	CISO
MDM-STD-009 is in no test and missing from MDM-D10 Section 5	An untested requirement was not reported as untested	GRC Analyst, for the next MDM-D10 revision

5. Reporting and Escalation

The dashboard is issued monthly to the people who own a decision or an action in it. A worse status is escalated within five working days, without waiting for the next issue.

5.1 Distribution and Cadence

A snapshot is issued on the 16th of each month, and once more within five working days after 14 February 2027 to report the retests. The GRC Analyst prepares it and the CISO approves it before it goes out (UR4).

Audience	Receives	Frequency	Purpose
CISO	Full Section 4	Monthly	Approves the snapshot and acts on the items for attention
Business Owner (Risk Owner)	Overall status, RM-06, RM-08 and the decisions due	Monthly	Tracks the open decisions and the residual risks they own
IT Operations Manager (Control Owner)	Control readiness, RM-09 and their own recommendations	Monthly	Tracks remediation against due dates
Internal Audit	Full Section 4	Quarterly	Independent view, and the status of MDM-REC-003 and MDM-REC-009, which it retests
Senior management	Overall status and summary, through MDM-D14	Quarterly	Readiness decision and support needed

Each snapshot states its as-at date, the simulated label, and what changed since the last one. Values are never shown without their status, so a reader does not have to judge a number alone.

5.2 Escalation

Condition	Escalated To	Within
The overall status gets worse	CISO and Business Owner	5 working days
An outcome measure (RM-07 to RM-09) turns Red	CISO	5 working days
A recommendation passes its due date	Risk Owner of the linked risk, as MDM-D12 Section 2.3 requires	5 working days
An event in MDM-D12 Section 6 occurs	Risk Owner, as MDM-D12 Section 6 requires. The dashboard is refreshed (UR3)	5 working days
An item for attention stays open past two monthly issues	CISO raises it with the Business Owner	At the third monthly issue

Escalation reports the condition and its source. The decision stays with the Risk Owner or the CISO, as set in MDM-D12.

The current items for attention (Section 4.5) are raised in the first issue. If D-01 or the next test cycle still has no date by the 16 January 2027 issue, the CISO raises it with the Business Owner.

6. Assumptions and Limitations

6.1 Assumptions

ID	Assumption
AS-01	MDM-D04 and MDM-D09 to MDM-D12 are current as at 16 November 2026. The dashboard holds no value they do not hold.
AS-02	The thresholds in Section 3 are set for this case study and its sample of ten tests. They are not taken from a standard.
AS-03	The retest dates in MDM-D12 Section 5 hold. The projections in Sections 4.1 and 4.4 assume every retest passes.
AS-04	The roles in Section 5 exist as described in MDM-D02 and MDM-D12, including the Business Owner and Internal Audit.

6.2 Limitations

ID	Limitation
LM-01	No tenant was configured and no dashboard tool was built. All values are

ID	Limitation
	simulated.
LM-02	The overall status covers the tested scope only. RM-01 to RM-03 show what lies outside it.
LM-03	The measures count items and do not weight them by risk. In RM-07, a test on a High risk counts the same as one on a Medium risk, so RM-07 is read with RM-08 and MDM-D12 Section 4.
LM-04	A control rating summarises its test results. The failed steps behind a Partial or Not Implemented rating are in MDM-D10 and MDM-D11.
LM-05	The counts in Section 4.2 were made by hand from MDM-D09 and MDM-D10. A change in either document requires a recount (UR1).
LM-06	Projections in Sections 4.1 and 4.4 are expectations, not results. They hold only after passed retests.
